(17)

1st AND PART BILL

Measurements Recorded On: 30-07-21 to 07-08-21

Sl. NO / BOQ NO	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
Item No. 77	Providing and laying flooring using prepolished, water cut/gang saw 19mm thick granite laid over bed of 20mm thick 1:4 cm & jointed with neat cement slurry mixed with pigment to mach shade of granite slabs including laying POP on finished surface and cleaning the surface, including the cost of all materials and labours etc., complete as per specifications. - using silver grey granite / Multy Red / Ruby Red / Black / HassanGreen Granite of width not less than 900mm,complete as per Specification and directions of the Engineer in charge.(Third Floor)									
	Measurements taken on Granite Works									
	Existing Degree College Building - Third Floor									
	Class Room 1	1	1	7.86		7.000	55.02	Sqm		
	Class Room 2	1	1	8.20		7.050	57.81	Sqm		
	Class Room 3	1	1	8.00		7.050	56.40	Sqm		
	Staff Room	1	1	3.90		7.000	27.30	Sqm		
	Class Room 4	1	1	8.20		7.000	57.40	Sqm		
	Class Room 5	1	1	8.02		7.000	56.14	Sqm		
	Class Room 6	1	1	8.20		7.000	57.40	Sqm		
	Class Room 7	1	1	9.00		7.000	63.00	Sqm		
		1	1	4.90		0.450	2.21	Sqm		
	Corridor	1	1	62.75		1.600	100.40	Sqm		
	Steps									
	Risers	6	1	1.60		0.150	1.44	Sqm		
	Treads	6	1	1.60		0.300	2.88	Sqm		
	Skirting									
	Class Room 1	1	1	7.86		0.10	0.79	Sqm		
		2	1	7.00		0.10	1.40	Sqm		
		1	1	7.86		0.10	0.79	Sqm		
	Class Room 2	1	1	8.20		0.10	0.82	Sqm		
		2	1	7.05		0.10	1.41	Sqm		
		1	1	8.20		0.10	0.82	Sqm		
	Class Room 3	1	1	8.00		0.10	0.80	Sqm		
		2	1	7.05		0.10	1.41	Sqm		
		1	1	8.00		0.10	0.80	Sqm		
	Staff Room	1	1	3.90		0.10	0.39	Sqm		
		2	1	7.00		0.10	1.40	Sqm		
		1	1	3.90		0.10	0.39	Sqm		
	Class Room 4	1	1	8.20		0.10	0.82	Sqm		
		2	1	7.00		0.10	1.40	Sqm		
		1	1	8.20		0.10	0.82	Sqm		
	Class Room 5	1	1	8.02		0.10	0.80	Sqm		
		2	1	7.00		0.10	1.40	Sqm		
		1	1	8.02		0.10	0.80	Sqm		
	Class Room 6	1	1	8.20		0.10	0.82	Sqm		
		2	1	7.00		0.10	1.40	Sqm		
		1	1	8.20		0.10	0.82	Sqm		
	Class Room 7	1	1	9.00		0.10	0.90	Sqm		
		2	1	7.00		0.10	1.40	Sqm		
		1	1	9.00		0.10	0.90	Sqm		
		1	1	4.90		0.10	0.49	Sqm		
		2	1	0.60		0.10	0.12	Sqm		

CONTRACTOR CONSULTANCY ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

SSR INFRATECH

8/9/21

Asst. Executive Engineer

Scanned by TapScanner

2nd AND PART BILL

Measurements Recorded On:

Sl. NO / BOQ NO	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
	Deduction									
	Door (D)	7	-0.5	1.20		0.100	-0.42	Sqm		
	Door (D1)	1	-0.5	0.90		0.100	-0.05	Sqm		
	Stage In Class Rooms									
	Platform	1	7	3.70		1.600	41.44	Sqm		
	Rises	2	7	3.70		0.300	15.54	Sqm		
	Rises	2	7	1.60		0.300	6.72	Sqm		
					Qty to be Paid		**624.74**	**Sqm**	2633.19	1645049.34

Chd. & fe.

DSR INFRATECH Date..... BENGALURU

CONTRACTOR

CONSULTANCY

ASSISTANT ENGINEER
8/9/21

ASSISTANT EXECUTIVE ENGINEER
Asst. Executive Engine

Scanned by TapScanner

2nd AND PART BILL

Measurements Recorded On: 15-3-21

Sl. NO / BOQ NO	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
Item No. 89	Fixing of door frames in an existing opening including embedding frame in floor and walls after cutting masonary for holdfasts for embedding holdfast in cement concrete 1:3:6 of 20mm and downsize granite metal painting two coats of coal tar to sides of frame,making good the damages to walls and floor as required and disposal of the debries with lead upto 50 m. including cost of materials, labour, complete as per specificationsand directions of the Engineer in charge.									
	Measurements taken on									
	Door Frames									
	Existing Degree College Building - Third Floor									
	Door (D1)	7	1				7	NO		
	Door (D2)	1	1				1	NO		
					Qty to be Paid		**8.00**	**NO**	1490.03	11920.26

DSR INFRA... BENGALURU Date.....

CONTRACTOR

CONSULTANCY

ASSISTANT ENGINEER

08/9/21

ASSISTANT EXECUTIVE ENGINEER

Asst. Executive Engineer

Project Division

Scanned by TapScanner

Scanned by TapScanner

2nd AND PART BILL

Measurements Recorded On:

Sl. NO / BOQ NO	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
Item No. 94	Providing and fixing in position fully panelled Honne wood shutters for doors, styles and rails of 40mm. thick with bottom and lock rails 180mm wide top rail and styles 100mm wide as per drawing and panels of 25mm thick including cost of materials, labour, HOM of machineries complete as per specifications. (excluding cost of fixtures)and directions of the Engineer in charge.(Third Floor)									
	Measurements taken on									
	Door Shutters									
	Existing College Building - Third Floor									
	Door (D)	1	7	1.05		1.95	14.33	Sqm		
	Door (D1)	1	1	0.75		1.95	1.46	Sqm		
					Qty to be Paid		**15.80**	Sqm	5163.85	81562.97

DSR INFRATECH
Date.....
BENGALURU

CONTRACTOR

CONSULTANCY

ASSISTANT ENGINEER
8/9/21

ASSISTANT EXECUTIVE ENGINEER
Asst. Executive Enginee

Scanned by TapScanner

(11)

1st AND PART BILL

Measurements Recorded On:

Sl. No / BOQ No	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	Qty	Unit	Rate	Amount
Item No. 111	Providing and fixing M.S.grill work for windows and ventilators weighing 21kg/sqm using M.S. flats, or M.S. square rods, or combination of M.S. flats and square rods as per approve design, drawing including cutting steel sections and welding the same to required pattern with a coat of red lead primer, cost of materials, fixtures, labour and HOM of machinery complete as per specificationsand directions of the Engineer in charge. (Second Floor)									
	Measurements taken on									
	MS Grill Works									
	Second Floor									
	Above Corridor Parapet Wall									
	Existing College Building (Second Floor									
	Window	1	8	3.5		1.5	42.00	Sqm		
	Window	1	5	3.33		1.5	24.98	Sqm		
	Window	1	1	1.33		1.5	2.00	Sqm		
	Window	1	1	0.83		1.5	1.25	Sqm		
							70.22	Sqm		
					Qty to be Paid		1685.16	KG		
					Qty Upto 125%		1685.16	KG	116.72	196684.46
					Qty Above 125%		0.00	KG	116.72	0.00

DSR INFRATECH Date.....

CONTRACTOR CONSULTANCY ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

Asst. Executive Engineer

Scanned by TapScanner

1ST AND FAKI BILL

Measurements Recorded On:

Sl. No. Book No. Page No.	Description of Item	No.	No.	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
Item No. 104	Providing and fixing M.S Grill over existing compound wall as per, using 16mm x 16mm M.S Square rod @ 150mm c/c spacing and 6mm x 40mm M.S. flats as horizontal and 6mm x12mm M.S. flat for ornamental design and providing chop edge design at the vertex of every vertical rods, including welding, grinding wherever necessary. All the steel surface should be thoroughly cleaned free of rust and painted with anti corrosive paint (shop paint) etc., complete. The work includes cost of all materials, labour charges for all items of work, hire charges for welding, cutting and grinding equipments, and electricity charges, etc., complete as per specifications and directions of the Engineer in charge. (First Floor)									
	Measurements taken on MS Grill Works.									
	Ground Floor									
	Door Verandah (D)	1	1	2.1		0.1	0.66	Sqm		
	Door Verandah (D1)	1	1	0.9		0.1	0.14	Sqm		
	Window (W1)	18	1	1.83		1.13	39.20	Sqm		
	Verandhas (V)	10	1	0.6		0.7	4.20	Sqm		
	At 1st Deck									
	Existing above culvert	1	1	9.20	0.81		7.45	Sqm		
	First Floor									
	Door Verandhas (D)	1	8	1.2		0.1	1.44	Sqm		
	Window (W1)	18	1	1.83		1.13	59.46	Sqm		
	Window (W2)	3	1	1.2		1.1	3.96	Sqm		
	At 1st Deck									
	Existing above culvert	1	1	9.20	0.81		7.45	Sqm		
	Above Corridor Parapet									
	Existing 1 college Building 1 Ground Floor									
	New Ground Floor staircase	1	1	1.8		1.25	2.25	Sqm		
		1	0.5	3.04		1.25	1.9	Sqm		
	Main Door entrance	1	1	4.86		1.5	16.94	Sqm		
	corridor window	1	1	3.5		1.5	5.25	Sqm		
	Right side of main entrance	1	1	3.3		1.5	4.95	Sqm		
	window	1	1	1.8		1.5	2.7	Sqm		
	Left side of main entrance	1	1	1.5		1.5	2.25	Sqm		
	Right side of main entrance	1	1	1.83		1.83	3.3489	Sqm		
	W indow	1	1	3.15		1.5	4.725	Sqm		
	W indow	1	1	3.45		1.5	5.18	Sqm		
	W indow	1	1	3.15		1.5	4.725	Sqm		
	W indow	3	1	1.8		1.5	13.50	Sqm		
	W indow	1	1	1.8		1.5	2.70	Sqm		
		1	1	1.5		1.5	2.25	Sqm		
	Existing 1 college Building 1 First Floor									
	W indow	1	8	3.8		1.5	45.648	Sqm		
	W indow	1	1	3.53		1.5	5.295	Sqm		
						Qty to be Paid	371.73	Sqm		
						Qty Upto 125%	65.08	Sqm		
						Qty Above 125%	229.65	Sqm		

Scanned by TapScanner

Scanned by TapScanner

2nd AND PART BILL

Measurements Recorded On:

Sl NO / BOQ NO	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
Item No. 118	Providing and fixing M.S.Grill over existing compound wall as per, using 16mm x 16mm M.S.Square rod at 150mm c/c spacing and 6mm x 40mm M.S. flats at horizontal and 6mm x12mm M.S. flat for ornamental design and providing shop edge design at the vertex of every vertical rods, including welding, grinding wherever necessary. All the steel surface should be thoroughly cleaned free of rust and painted with anti corrosive paint (shop paint) etc., complete. The work includes cost of all materials, labour charges for all items of work, hire charges for welding, cutting and grinding equipment, and electricity charges, etc., complete as per specification and directions of the Engineer in charge. (Third Floor)									
	Measurements taken on									
	MS Grill Works									
	Third Floor									
	Door Ventelator(D1)	1	4	1.2		0.3	1.44	Sqm		
	Window (W1)	18	1	1.8		1.5	48.60	Sqm		
	Window (W2)	2	1	1.2		1.5	50.04	Sqm		
	Cut Out									
	Grating above cutout parapet	1	1	9.20	0.81		7.45	Sqm		
	Terrace Floor									
	Cut Out									
	Grating above cutout parapet	1	1	9.20	0.81		7.45	Sqm		
	Existing Degree College Building - Third Floor									
	Window (W1)	30	1	1.8		1.5	81.00	Sqm		
	Door Ventilator (D)	7	1	1.2		0.3	2.52	Sqm		
	Door Ventilator (D1)	1	1	0.9		0.3	0.27	Sqm		
	Above Corridor Parapet Wall									
	Existing College Building - Third Floor									
	Corridor - Long Wall	1	1	63.05		3.10	195.46	Sqm		
	Corridor - Short wall (Sides)	2	1	1.60		3.10	9.92	Sqm		
					Qty to be Paid		**404.15**	**Sqm**		
					Qty Upto 125%		**177.34**	**Sqm**	5876.14	1042059.91
					Qty Above 125%		**226.81**	**Sqm**	5876.14	1332776.04

OSR INFRATECH
Date.....

CONTRACTOR

CONSULTANCY

ASSISTANT ENGINEER
8/9/21

ASSISTANT EXECUTIVE ENGINEER
Asst. Executive Engineer
Project Division
8/9/2021

Scanned by TapScanner

3RD X-NIS PART BILL

Measurements Recorded On:

Sl. No.	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
	Fabricating, supplying and erecting M.S. Pratt/Warren of span upto 10m. The bottom and top member is provided with 65x65x6mm double equal angles, welded back to back and in between top and bottom line. In webs of said section is provided with 50x50x6mm equal angle angle the vertical and inclined members and at supporting ends 80x80x8mm angle angle is provided. All the members are welded together with 8mm gusset plate as per Drawing. The entire truss is anchored in RCC column by using 4 Nos. of M.S. anchor bolts at each support, with 10mm thick base plate and shoe plate. The work includes cutting, straightening, placing in position of M.S angle and welding wherever necessary, and applying one coat of red oxide primer coat to all themembers including cost of all materials, labour charges, and hire charges of machineries for cutting, welding, grinding and erection equipments, with all lead and lift, transportation, etc., complete as per specification and directions of the Engineer in charge.									
	Measurements taken on MS tubular Truss Works									
	Existing Degree College Building - Third Floor					unit weight kg/m				
	Purlins 60x60x4.8 mm	1	18.0	66.95		7.85	9460.04	kg		
	Battens(132x132x5.4mm)	1	35	16.40		20.88	7600.32	kg		
					Qty to be Paid		**17060.4**	**KG**	140.71	2400617.145

Ch. A f.L.

DSR INFRATECH BENGALURU

CONTRACTOR

CONSULTANCY

ASSISTANT ENGINEER

8/9/21

ASSISTANT EXECUTIVE ENGINEER

Asst. Executive Engineer
Project Division

Scanned by TapScanner

2ND AND PART BILL

Measurements Recorded On:

Sl. No/ BOQ No	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
Item No. 177	Puffed panel (Data Rate)Lightweight, energy-efficient and durable panels , PUF panels consist of a rigid core sandwiched between sheet metal structural boards. PUF insulated sandwich panels integrate joists and studs, insulation, vapor and air barriers. complete as per specificationsand and directions of the Engineer in charge.									
	Measurements taken on PUF Panels									
	RA BILL 2									
	Existing Degree College									
		1	1	66.95		10.40	696.28	Sqm		
					Qty to be Paid		696.28	Sqm		
					Qty Upto 125%		696.28	Sqm	4242.00	2953619.76

CHK. & Fe

CONTRACTOR

CONSULTANCY

ASSISTANT ENGINEER
8/9/21

ASSISTANT EXECUTIVE ENGINEER
Asst. Executive Engine
Project Division

Scanned by TapScanner

2ND AND PART BILL

Measurements Recorded On:

Sl. NO / BOQ NO	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
Item No. 128	Applying red lead ready mix priming coat over new steel or other metal surface including preparing the surface after throughly cleaning oil, grease, dirt and other foreign matter, and scoured with wire brushes, fine steel wool, sand papers including cost of materials, labour, complete as per specifications and directions of the Engineer in charge.									
	Measurements taken on									
	Priming Coat over Steel									
	Existing Degree College Building- Third Floor				PERIMETER					
	Purlins 60x60x4.8 mm	1	18.0	66.95	0.24		289.22	Sqm		
	Battens(132x132x5.4mm)	1	35	10.40	0.264		96.10	Sqm		
					Qty to be Paid		**385.32**	**Sqm**	44.72	17232.59

DSR INFRATECH Date..... BENGALURU

CONTRACTOR

CONSULTANCY

ASSISTANT ENGINEER
8/9/21

ASSISTANT EXECUTIVE ENGINEER
Asst. Executive Engine
Project Division
8/9/2021

Scanned by TapScanner

2nd AND PART BILL										
Measurements Recorded On:										
Sl. NO / BOQ NO	**Description of Item**	**No**	**No**	**Length (m)**	**Breadth (m)**	**Depth (m)**	**QTY**	**Unit**	**Rate**	**Amount**
Item No. 129	Providing & Fixing of Mineral Fibre Suspended Ceiling System in the module size of 600x600x19mm with exposed grid. The tiles should have Humidity Resistance(RH) of 99%, Light Reflectance 87%, Thermal conductivity k=0.052-0.057w/m K,NRC-0.7, colour white, Fire Performance UK A2 S1, do with antimicrobial coating on the face of the tile, suitable for zone 4 area according to NF S 90-35:2003 with clean room clss of ISO 5(class 100), Decontamination class of CP10 and Bactoriological cleanlines class B1 for specific strains and reduction in colony size. Washability properties of 500 wash cycles as per ASTM D-4828 and suitable for Green Building application with Recycled content of 37%. The tile shall be laid on 24mm wide T-section flanges colour white having rotary stitching on all t sections i.e. the main runner, 1200mm & 600mm cross tees with web height f 38mm and a load carrying sections should have a galvanizing of 90grmas per sqm and need to be installed with suspension system of approved make.complete as per specifications and directions of the Engineer in charge.									
	Measurements taken on									
	False Ceiling in Classrooms									
	Existing Degree College Building - Third Floor									
	Class Room 1	1	1	7.86		7.000	55.02	Sqm		
	Class Room 2	1	1	8.20		7.050	57.81	Sqm		
	Class Room 3	1	1	8.00		7.050	56.40	Sqm		
	Staff Room	1	1	3.90		7.000	27.30	Sqm		
	Class Room 4	1	1	8.20		7.000	57.40	Sqm		
	Class Room 5	1	1	8.02		7.000	56.14	Sqm		
	Class Room 6	1	1	8.20		7.000	57.40	Sqm		
	Class Room 7	1	1	9.00		7.050	63.45	Sqm		
		1	1	4.90		0.600	2.94	Sqm		
	Corridor	1	1	62.75		1.600	100.40	Sqm		
					Qty to be Paid		**534.26**	**Sqm**	2709.55	1447602.69

DSR INFRATECH
Date.....

CONTRACTOR

CONSULTANCY

ASSISTANT ENGINEER
8/9/21

ASSISTANT EXECUTIVE ENGINEER
Asst. Executive Engineer
Project Division

Scanned by TapScanner

2nd AND PART BILL

Measurements Recorded On:

Sl. NO / BOQ NO	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
Item No. 120	Providing & Fixing of Mineral Fibre Suspended Ceiling System in the module size of 600x600x19mm with exposed grid. The tiles should have Humidity Resistance(RH) of 99%, Light Reflectance 87%, Thermal conductivity k=0.052-0.057w/m K,NRC-0.7, colour white, Fire Performance UK A2 S1, do with antimicrobial coating on the face of the tile, suitable for zone 4 area according to NF S 90-35:2003 with clean room clss of ISO 5(class 100), Decontamination class of CP10 and Bactoriological cleanlines class B1 for specific strains and reduction in colony size. Washability properties of 500 wash cycles as per ASTM D-4828 and suitable for Green Building application with Recycled content of 37%. The tile shall be laid on 24mm wide T-section flanges colour white having rotary stitching on all t sections i.e. the main runner, 1200mm & 600mm cross tees with web height f 38mm and a load carrying sections should have a galvanizing of 90grmas per sqm and need to be installed with suspension system of approved make.complete as per specifications and directions of the Engineer in charge.									
	Measurements taken on									
	False Ceiling in Classrooms									
	Existing Degree College Building - Third Floor									
	Class Room 1	1	1	7.86		7.000	55.02	Sqm		
	Class Room 2	1	1	8.20		7.050	57.81	Sqm		
	Class Room 3	1	1	8.00		7.050	56.40	Sqm		
	Staff Room	1	1	3.90		7.000	27.30	Sqm		
	Class Room 4	1	1	8.20		7.000	57.40	Sqm		
	Class Room 5	1	1	8.02		7.000	56.14	Sqm		
	Class Room 6	1	1	8.20		7.000	57.40	Sqm		
	Class Room 7	1	1	9.00		7.050	63.45	Sqm		
		1	1	4.90		0.600	2.94	Sqm		
	Corridor	1	1	62.75		1.600	100.40	Sqm		
					Qty to be Paid		**534.26**	**Sqm**	2709.55	1447602.69

DSR INFRATECH
Date.....

CONTRACTOR

CONSULTANCY

ASSISTANT ENGINEER
8/9/21

ASSISTANT EXECUTIVE ENGINEER
Asst. Executive Engineer
Project Division

Scanned by TapScanner

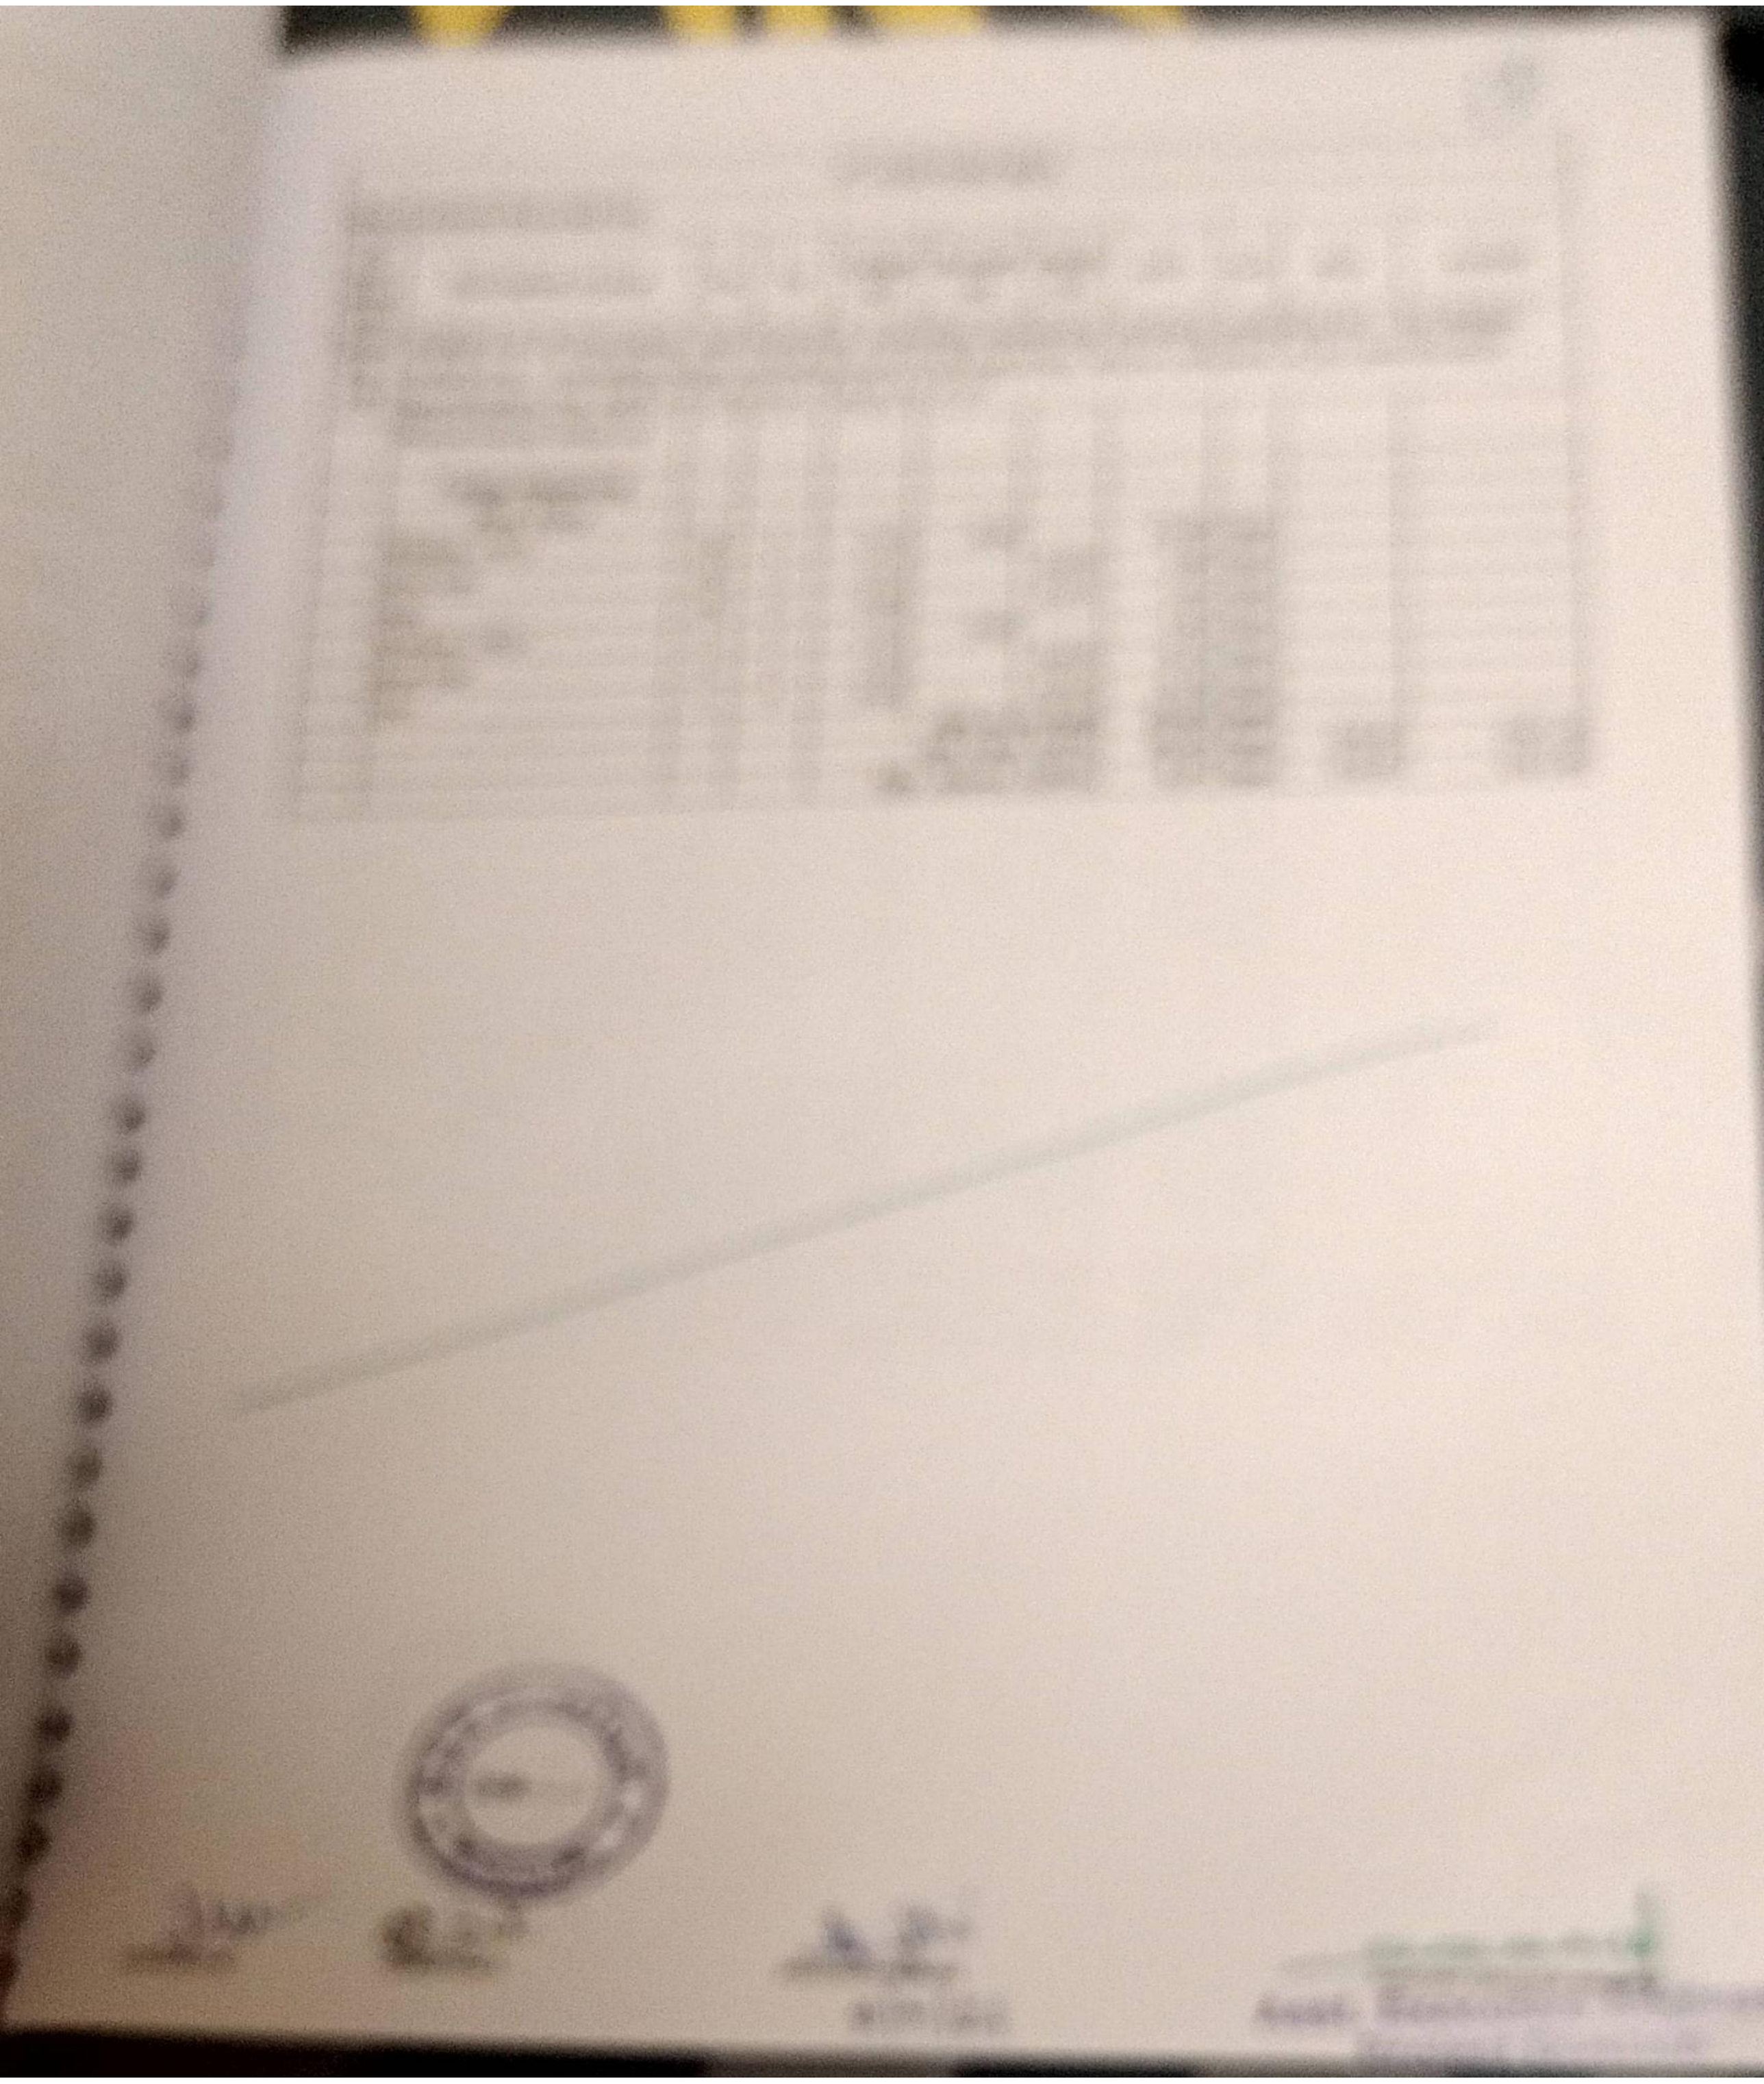

Scanned by TapScanner

3rd AND PART BILL

Measurements Recorded On:

Sl. NO / BOQ NO	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
Item No. 229	Providing and removing centering, shuttering, strutting, propping etc., for chajjas, corbels etc., including edges including cost of all materials, labour complete as per specification and directions of the Engineer in charge (second Floor)									
	Measurements taken on									
	Chajja Shuttering									
	Second Floor									
	Window (W1)	18	1	2.13	0.60		23.00	Sqm		
	front side	18	1	2.13		0.075	2.88	Sqm		
	side	18	2	0.60		0.075	1.62	Sqm		
	Window (W2)	2	1	1.50	0.60		1.80	Sqm		
	front side	2	1	1.50		0.075	0.23	Sqm		
	side	1	4	0.60		0.075	0.18	Sqm		
	Chajja									
	Third Floor									
	Window (W1)	18	1	2.12	0.60		22.90	Sqm		
	front side	18	1	2.12		0.075	2.86	Sqm		
	side	18	2	0.60		0.075	1.62	Sqm		
	Window (W2)	2	1	1.50	0.60		1.80	Sqm		
	front side	2	1	1.50		0.075	0.23	Sqm		
	side	1	4	0.60		0.075	0.18	Sqm		
	Existing Degree College Building - Third Floor									
	Chajja									
	Window (W1)	15	1	2.12	0.60		19.08	Sqm		
	front side	15	1	2.12		0.075	2.39	Sqm		
	side	1	30	0.60		0.075	1.35	Sqm		
					Qty to be Paid		82.10	Sqm		
					Qty Upto 125%		20.25	Sqm	365.42	7399.71
					Qty Above 125%		61.85	Sqm	365.42	22602.02

DSR INFRATECH
Date
AE/AP

CONTRACTOR

CONSULTANCY

ASSISTANT ENGINEER
8/9/21

ASSISTANT EXECUTIVE ENGINEER
Asst. Executive Engr
Project Division
Yelahanka Zone

Scanned by TapScanner

2nd AND PART BILL

Measurements Recorded On:

Sl. NO / BOQ NO	Description of Item	No	No	Length (m)	Breadth (m)	Depth (m)	QTY	Unit	Rate	Amount
Item No. 242	Providing lime rendering for plastering to wall and ceiling, including cost of materials, labour, curing complete as per specifications and directions of the Engineer in charge (head room)									
	Measurements taken on									
	Lime Rendering to Walls									
	Existing Degree College Building - Third Floor									
	Class Room 1	1	1	7.86		4.57	35.94	Sqm		
		2	1	7.00		4.34	60.81	Sqm		
		1	1	7.86		4.11	32.34	Sqm		
	Class Room 2	1	1	8.20		4.57	37.49	Sqm		
		2	1	7.05		4.34	61.24	Sqm		
		1	1	8.20		4.11	33.74	Sqm		
	Class Room 3	1	1	8.00		4.57	36.58	Sqm		
		2	1	7.05		4.34	61.24	Sqm		
		1	1	8.00		4.11	32.92	Sqm		
	Staff Room	1	1	3.90		4.57	17.83	Sqm		
		2	1	7.00		4.34	60.81	Sqm		
		1	1	3.90		4.11	16.05	Sqm		
	Class Room 4	1	1	8.20		4.57	37.49	Sqm		
		2	1	7.00		4.34	60.81	Sqm		
		1	1	8.20		4.11	33.74	Sqm		
	Class Room 5	1	1	8.02		4.57	36.67	Sqm		
		2	1	7.00		4.34	60.81	Sqm		
		1	1	8.02		4.11	33.00	Sqm		
	Class Room 6	1	1	8.20		4.57	37.49	Sqm		
		2	1	7.00		4.34	60.81	Sqm		
		1	1	8.20		4.11	33.74	Sqm		
	Class Room 7	1	1	9.00		4.57	41.15	Sqm		
		2	1	7.00		4.34	60.81	Sqm		
		1	1	9.00		4.11	37.03	Sqm		
		1	1	4.90		4.570	22.39	Sqm		
		2	1	0.60		4.340	5.21	Sqm		
	Deduction									
	Door (D)	7	-0.5	1.20		2.400	-10.08	Sqm		
	Door (D1)	1	-0.5	0.90		2.400	-1.08	Sqm		
	Window	30	-0.5	1.83		1.530	-42.00	Sqm		
					Qty to be Paid		**994.97**	**Sqm**		
					Qty Upto 125%		**104.29**	**Sqm**	54.54	5687.84
					Qty Above 125%		**890.68**	**Sqm**	54.54	48577.70

DSR INFRATECH BENGALURU Date.....

CONTRACTOR CONSULTANCY ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

8/9/21 8/9/2021

Scanned by TapScanner

Scanned by TapScanner
